



**FOR IMMEDIATE RELEASE
MAY 8, 2015**

MEDIA CONTACT
816-804-8882
info@kcstreetcar.org

Streetcar Construction on Track Project Remains on Schedule, Budget

Kansas City, Missouri – Streetcar construction remains on schedule and on budget, with all key construction activities at least 70 percent complete.

"The project is really on the home-stretch," stated Meghan Jansen, public information manager for KC Streetcar Constructors. "Most of the underground work will be completed this month. That includes the upgrades to Kansas City's century-old water and sewer lines."

As of May 1, 2015:

- 71% of track is fully constructed (15,430 feet complete out of 21,771 total feet)
- 96% of water and sewer replacements and upgrades is complete
- 77% of work on the Singleton Yard vehicle maintenance facility is complete
- More than 100 power poles are installed
- First streetcar stop is built at 16th and Main

Streetcar construction is on schedule to be completed in fall of 2015. The streetcar system will then undergo a period of testing and is anticipated to be open to the public in 2016.


For more information, contact the KC Streetcar office at info@kcstreetcar.org or 816-804-8882. Updates available on www.kcstreetcar.org, Twitter ([@kcstreetcar](https://twitter.com/kcstreetcar)) and Facebook ([KC Streetcar](https://www.facebook.com/kcstreetcar)).

###




KC Streetcar Construction Progress | May 1, 2015


Utilities (Water & Sewer)

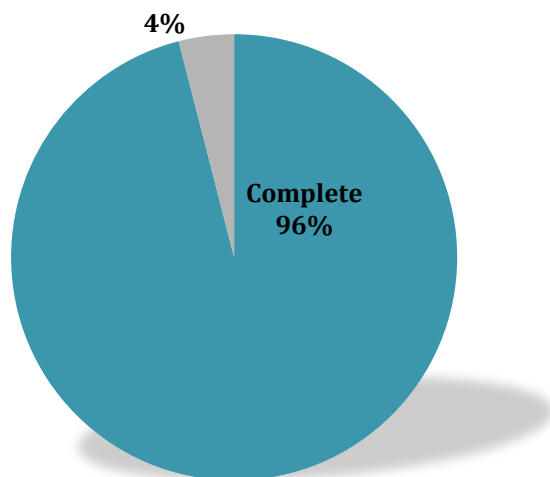

Track

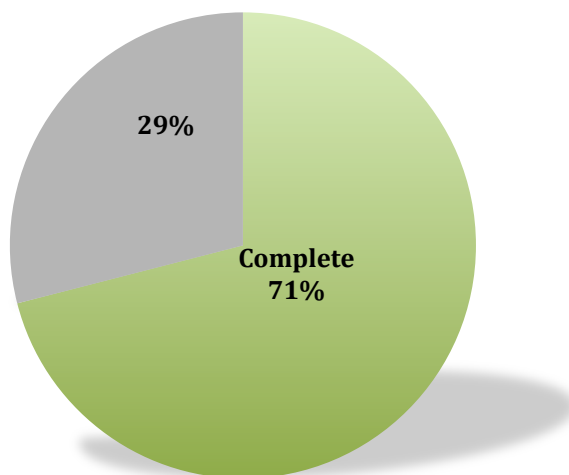

Singleton Yard (Vehicle Maintenance Facility)

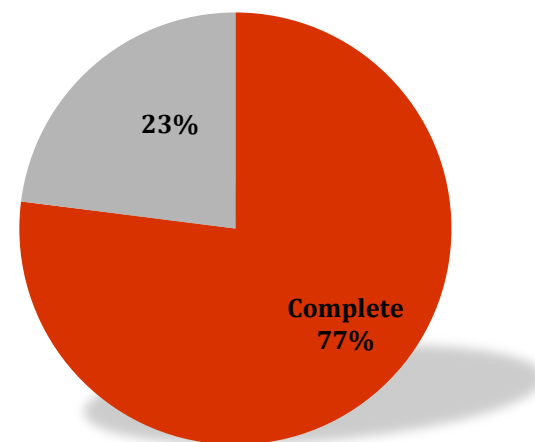

Progress of key areas of work as of May 1, 2015

KC  STREETCAR™

